



China

Pre-Shipment-Inspection Report No: 70.199.7.014.089

(1) AQL Result:

	Level I			Level S2		
	Accept / Reject	Actual Findings	Result	Accept / Reject	Actual Findings	Result
Critical Defective	Not Allowed	0	Pass	Not Allowed	0	Pass
Major Defective	01 / 02	0	Pass	00 / 01	0	Pass
Minor Defective	02/ 03	1	Pass	00 / 01	0	Pass

(2) Component check

Result: Pass

The components of the appliance were checked and found to comply with the certificate no. S 50076241 released by TUV-RL.

(3) Rating label

Result: Pass

-See attached photos

(4) Documents & Sample provided by client:

a) LVD Declaration of Conformity	<input checked="" type="checkbox"/>	Available	<input type="checkbox"/>	Not available	<input type="checkbox"/>	N/A
b) LVD report	<input checked="" type="checkbox"/>	Available	<input type="checkbox"/>	Not available	<input type="checkbox"/>	N/A
c) GS Certificate.	<input checked="" type="checkbox"/>	Available	<input type="checkbox"/>	Not available	<input type="checkbox"/>	N/A
d) Construction Data Form.	<input checked="" type="checkbox"/>	Available	<input type="checkbox"/>	Not available	<input type="checkbox"/>	N/A
e) EMC : D.O.C.	<input checked="" type="checkbox"/>	Available	<input type="checkbox"/>	Not available	<input type="checkbox"/>	N/A
f) EMC : Test report.	<input checked="" type="checkbox"/>	Available	<input type="checkbox"/>	Not available	<input type="checkbox"/>	N/A
g) Operation/ Instruction manual	<input type="checkbox"/>	Available	<input checked="" type="checkbox"/>	Not available	<input type="checkbox"/>	N/A
h) Installation Manual	<input type="checkbox"/>	Available	<input checked="" type="checkbox"/>	Not available	<input type="checkbox"/>	N/A
i) Sample	<input type="checkbox"/>	Available	<input checked="" type="checkbox"/>	Not available	<input type="checkbox"/>	N/A

(5) Defect

Result: N/A

N/A

(6) General Remarks:

6.1 We did not get any document from the client. Some photos of the product were taken for your information.



China

Pre-Shipment-Inspection Report No: 70.199.7.014.089

D. MASTER CHECKLIST

a. Sampling Level I

Categories	Inspection Items	Defective Description	Cri	Maj	Min
1. Safety Test	a. Hi-pot test (with 1800V/1s for class I items)	P			
	b. Hi-pot test (with 4000V/1s for class II items)	N/A			
	c. Earth continuity test (less than 0.1Ω, at 25 A)	P			
2. Marking	a. "CE" mark (height : min 5mm.)	P			
	b. "GS" mark	N/A			
	c. Trademark / manufacturer identification / rating label	P			
	d. Marking is reliable, damage or loosen	P			
	e. Technical parameter (voltage / wattage) refer to certificate / specification.	P			
3. Function	a. On/Off, or speed, or light control switch (not function)	P			
	b. Abnormal noise, or vibration	P			
	c. Machine malfunction / machine operated properly	P			
4. Wattage	a. less than or greater than specified limit	N/A			
5. Cosmetic / Appearance / Assembly	a. Dirt mark /scratch mark / poor finishing /silk screening / mould mark / flash on unit	-Oil on unit.			1
	b. Body deformed, crack, damage,	P			
	c. switches / control / knobs / screw etc.	P			
	d. Plug / Supply Cord (loosen / broken)	P			
	e. Foreign material inside	P			
	f. Front, Back, Side Housing (gap/ not tight/ not align)	P			
6. Accessory	a. Remote control provided	N/A			
	b. missing or damage of parts /components/ instruction manual /warrantee card /instruction leaflet / supply cord /others	P			
7. Packing	a. Wrong Packing	P			
	b. Gift box / PVC BAG / Carton Box (damage) , Printing on six faces (wrong/poor)	P			
Total			0	0	1

b. Sample Level S2

Categories	Inspection Items	Defective Description	Cri.	Maj	Min
1. Internal construction (visual check)	a. Symbol are not corrective (Live / Neutral / Earthing)	P			
	b. Cold soldering, soldering joints loosen	P			
	c. Loosen parts (switch, motor, control etc.)	P			
	d. Strain relief loosen	P			
Total			0	0	0

P -- Pass / F--Fail / N/A -- Not Applicable.

Appendix: Yes 4 pages, No


~ End of report ~



China

Pre-Shipment-Inspection Report No: 70.199.7.014.089

Attached photos

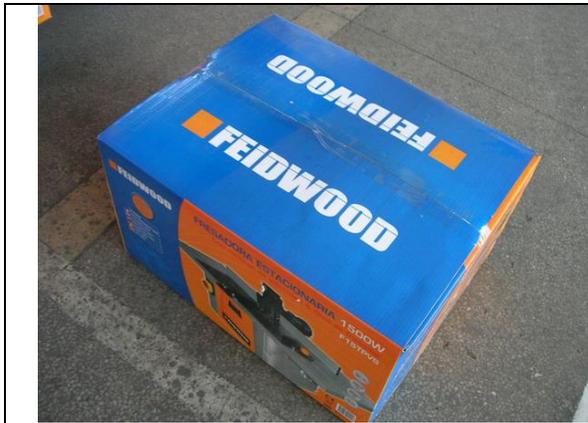


Export carton



Color box



Color box

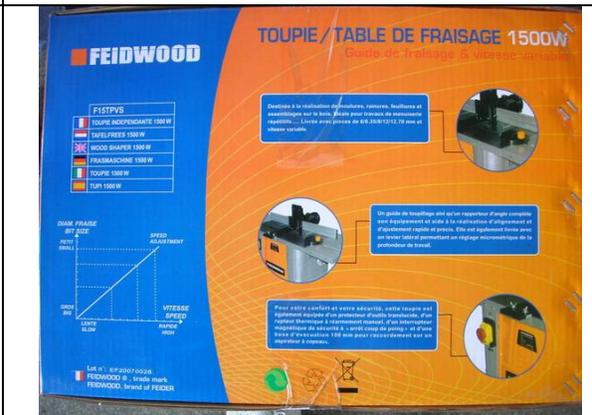

Color box



Barcode



Marking on color box



China

Pre-Shipment-Inspection Report No: 70.199.7.014.089

<p>Batch No</p>	<p>Packing</p>
<p>Product and accessories</p>	<p>Side of product</p>
<p>Side of product</p>	<p>Side of product</p>



China

Pre-Shipment-Inspection Report No: 70.199.7.014.089



Side of product




Logo




Rating label



Speed label

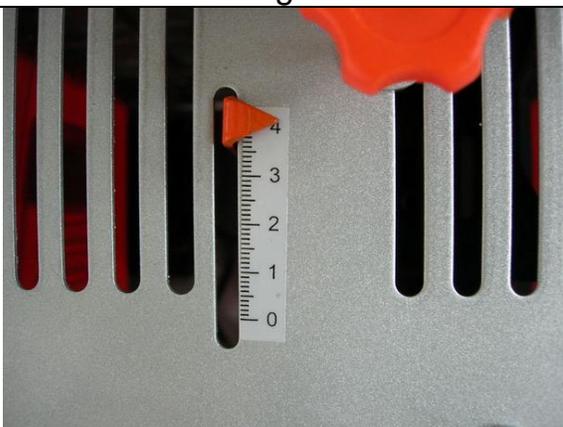

Depth label


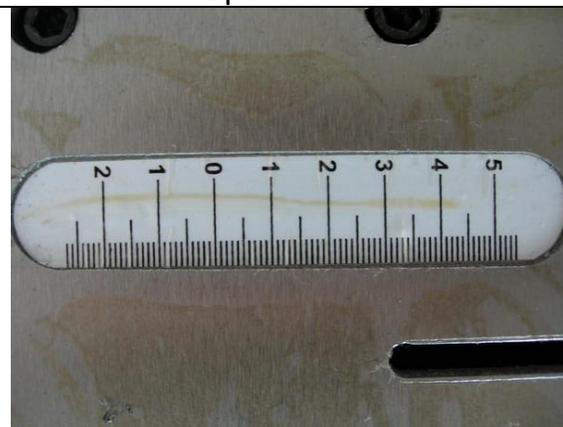


Label



China

Pre-Shipment-Inspection Report No: 70.199.7.014.089

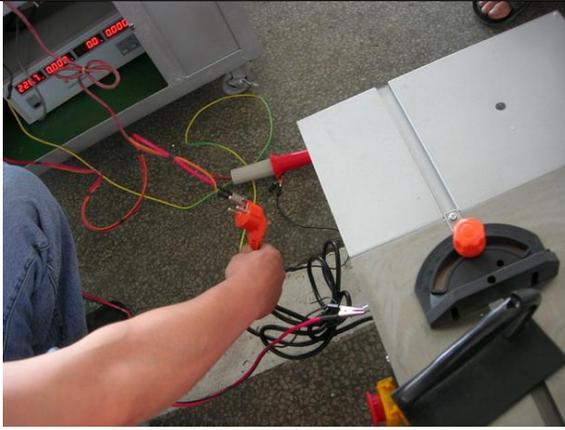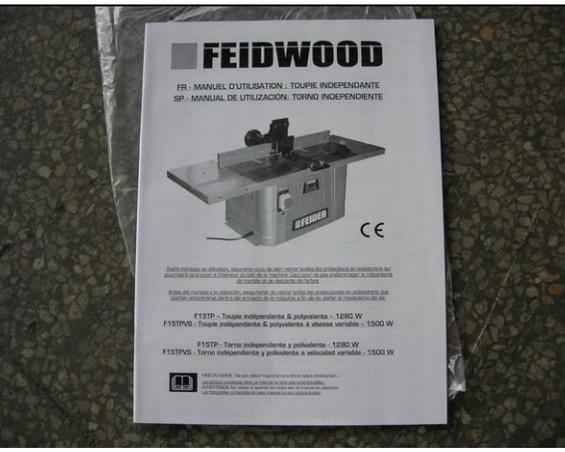	
<p>Hi-pot test</p>	<p>Earth continuous test</p>
	
<p>Construction check</p>	<p>I/M</p>
